


1. COUNTY Crawford CHECK ONE  Town  Village  City NAME Brideport

2. LOCATION (Number and Street or 1/4 section, section, township and range. Also give subdivision name, lot and block numbers when available) Sec. 18 Town 6-7N. Range 6-7W.

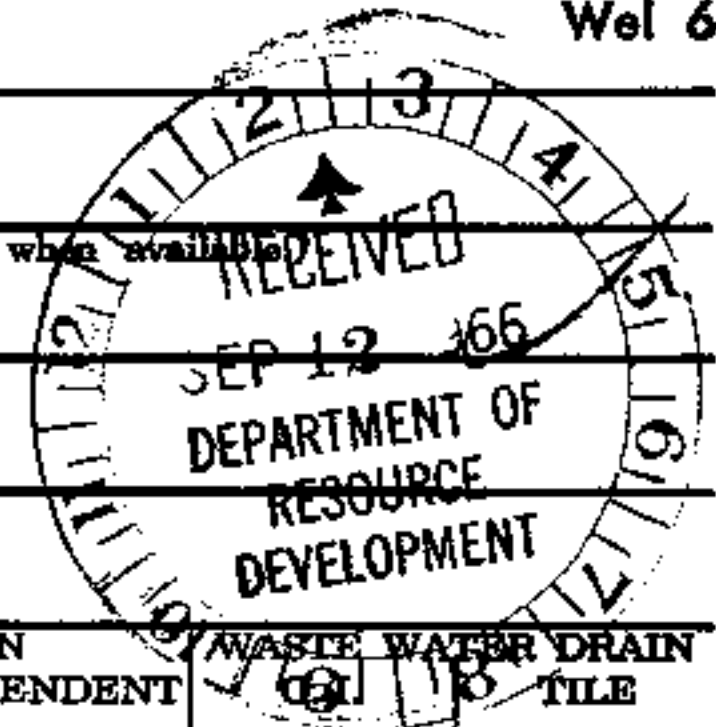

3. OWNER AT TIME OF DRILLING Glen Beneker

4. OWNER'S COMPLETE MAIL ADDRESS Prairie Du Chien, Wisconsin

5. Distance in feet from well to nearest:

BUILDING	SANITARY SEWER	FLOOR DRAIN	FOUNDATION DRAIN	WASTE WATER DRAIN
C. I.	C. I.	C. I.	SEWER CONNECTED	INDEPENDENT
6	200'			

CLEAR WATER DRAIN	SEPTIC TANK	PRIVY	SEEPAGE PIT	ABSORPTION FIELD	BARN	SILLO	ABANDONED WELL	SINK HOLE
C. I.	TILE							
	200'			250'	70'			

OTHER POLLUTION SOURCES (Give description such as dump, quarry, drainage well, stream, pond, lake, etc.)

6. Well is intended to supply water for: Farm

7. DRILLHOLE						10. FORMATIONS		
Dia. (in.)	From (ft.)	To (ft.)	Dia. (in.)	From (ft.)	To (ft.)	Kind	From (ft.)	To (ft.)
6"	Surface	128				Top soil and clay	Surface	20
						Sand and Gravel	20	80

8. CASING, LINER, CURBING, AND SCREEN			
Dia. (in.)	Kind and Weight	From (ft.)	To (ft.)
6	steel 19.45	Surface	100

9. GROUT OR OTHER SEALING MATERIAL		
Kind	From (ft.)	To (ft.)
	Surface	

Well construction completed on 8/29 1966

11. MISCELLANEOUS DATA

Yield test: 10 2 Hrs. at 10 GPM Well is terminated 10 inches  above  below final grade

Depth from surface to normal water level 36 ft. Well disinfected upon completion  Yes  No

Depth to water level when pumping 36 ft. Well sealed watertight upon completion  Yes  No

Water sample sent to Madison laboratory on: 8/29 1966

Your opinion concerning other pollution hazards, information concerning difficulties encountered, and data relating to nearby wells, screens, seals, type of casing joints, method of finishing the well, amount of cement used in grouting, blasting, sub-surface pumphrooms, access pits, etc., should be given on reverse side.

SIGNATURE Duane Lubbers Registered Well Driller COMPLETE MAIL ADDRESS Farmersburg, Iowa

Please do not write in space below

COLIFORM TEST RESULT	GAS - 24 HRS.	GAS - 48 HRS.	CONFIRMED	REMARKS
322				
